




Jury Management System AgileJury Version 4.4

Superior Court of Arizona in Maricopa County

August 2017

Agenda

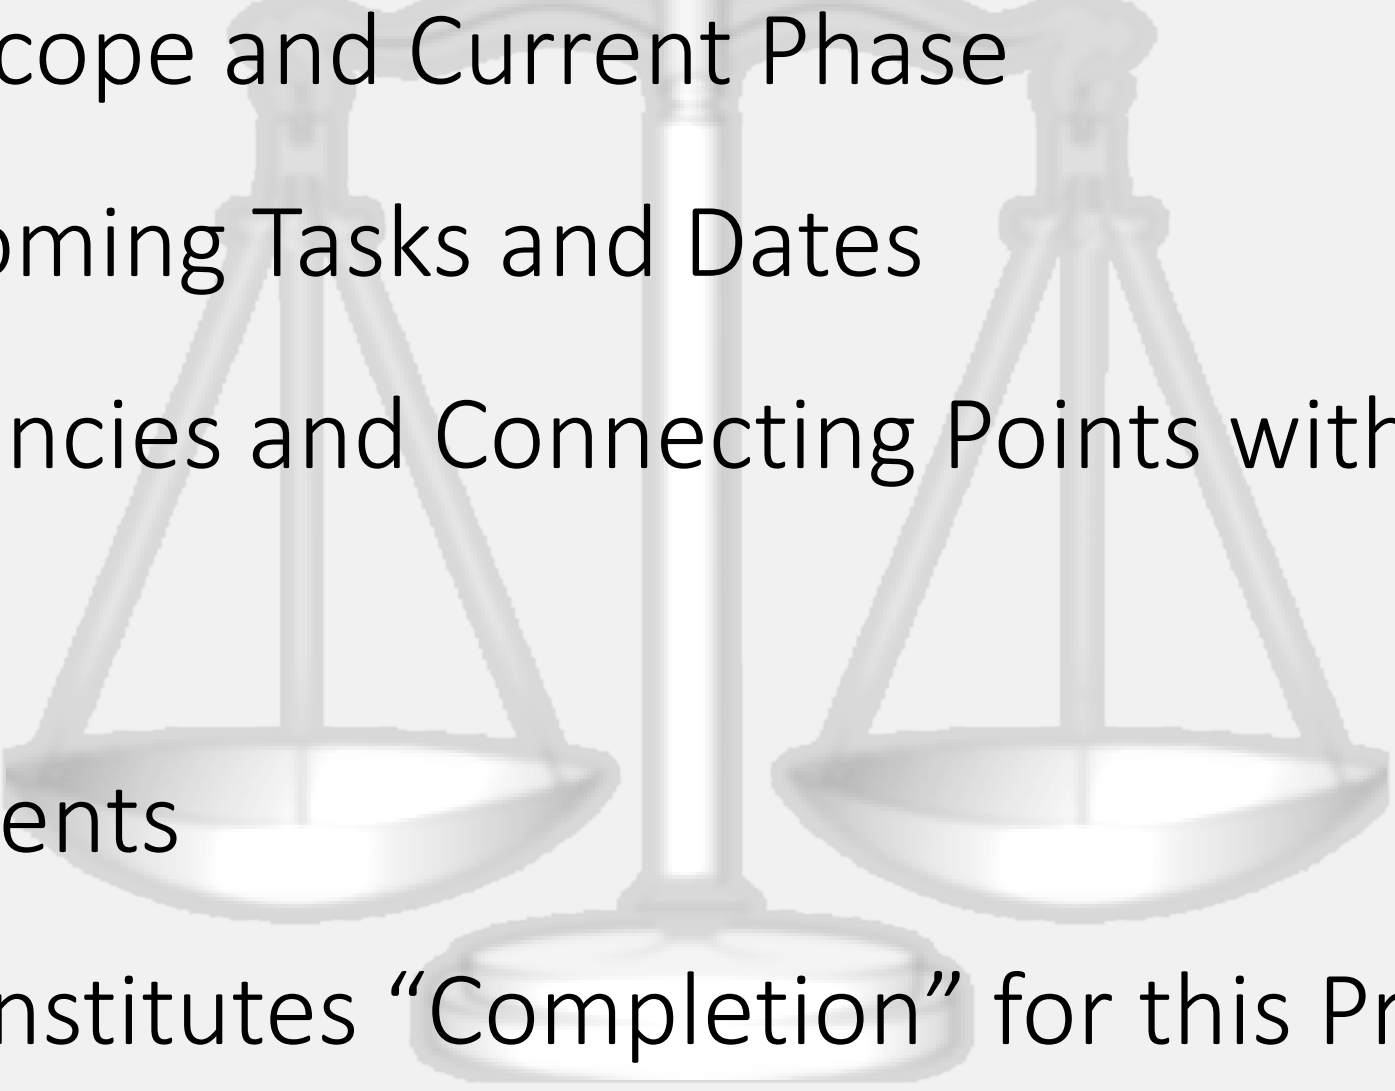- Project Scope and Current Phase
 - Key Upcoming Tasks and Dates
 - Dependencies and Connecting Points with Other Projects
 - Impediments
 - What Constitutes “Completion” for this Project
 - Planned Completion Date
- 


AgileJury 4.4 Scope – Maricopa County

➤ AgileJury Benefits

- Database table conversion providing the ability to change information (juror screens/postcards) without requiring a code change or assistance from vendor.
- Enhanced communication options with jurors (phone, email and text)
- Ability for juror to upload documents via web instead of submitting a request online
- Ability to upload and download NCOA, Death List, MVD/Elections files which are currently external to the application (perform NCOA prior to each summons mailing)
- Enhanced speed of application
- Enhanced data reporting

➤ Current Phase

➤ Development

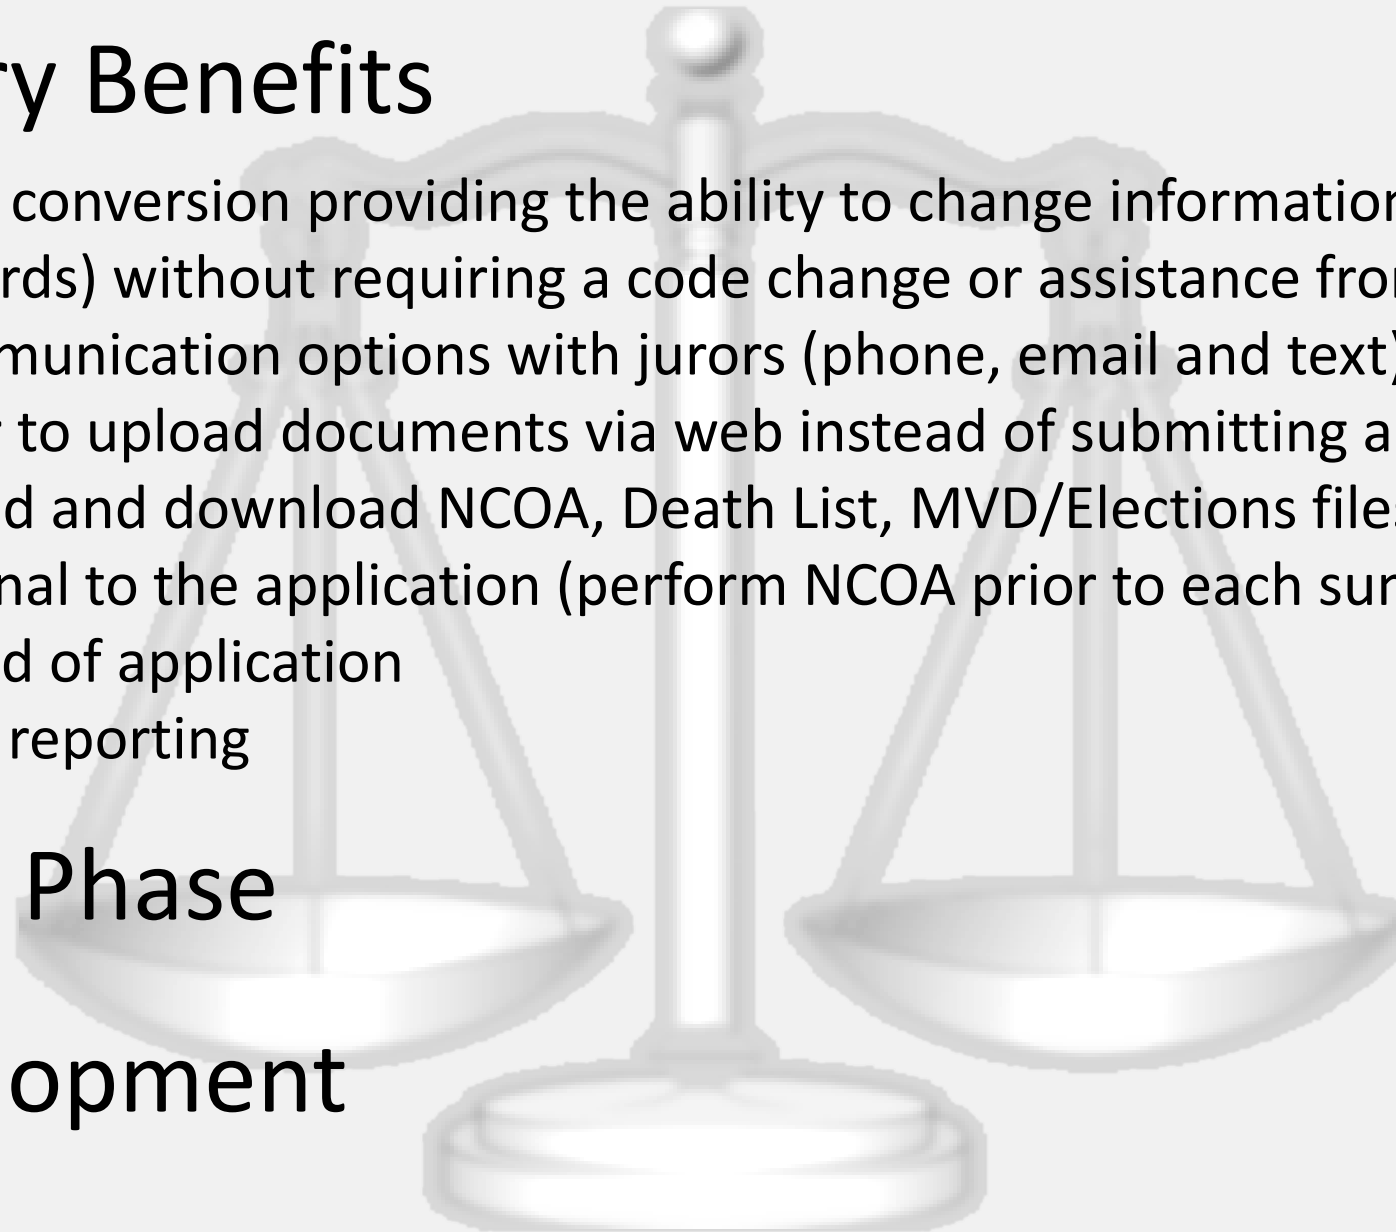

Key Upcoming Tasks and Dates


Task	Duration	Start	Finish
Code Development	85 Days	7/3/2017	10/27/2017
Sprint 2	20 Days	7/3/2017	7/28/2017
Sprint 3	25 Days	7/31/2017	9/1/2017
Hardening	20 Days	9/4/2017	9/29/2017
Code Drops	114 Days	10/30/2017	4/5/2018
User Testing	105 Days	11/20/2017	4/13/2018
Implementation	112 Days	11/8/2017	4/13/2018
Installation (Test)	106 Days	11/8/2017	4/5/2018
Code 1 Installation	0 Days	11/8/2017	11/8/2017
Code 2 Installation	0 Days	1/17/2018	1/17/2018
Code 3 Installation	0 Days	2/28/2018	2/28/2018
Code 4 Installation	0 Days	4/5/2018	4/5/2018
Training (Core Team)	5 Days	11/13/2017	11/17/2017
Go Live (multiple activities)	10 Days	4/13/2018	4/20/2018

Dependencies and Other Projects

- Tablet Code Drop must be installed and tested
 - Target date for installation (TBD)
 - Utilization of Kiosks (TBD)
 - Reports (TBD)
 - Need to be tested with AgileJury 4.4
- IVR Testing with AgileJury 4.4 (OET)
 - Need Code Development (OET)

Possible Impediments

- Need successful implementation of Tablet Code Drop
- Code Development (if Kiosks are used)
- All reports must successfully execute

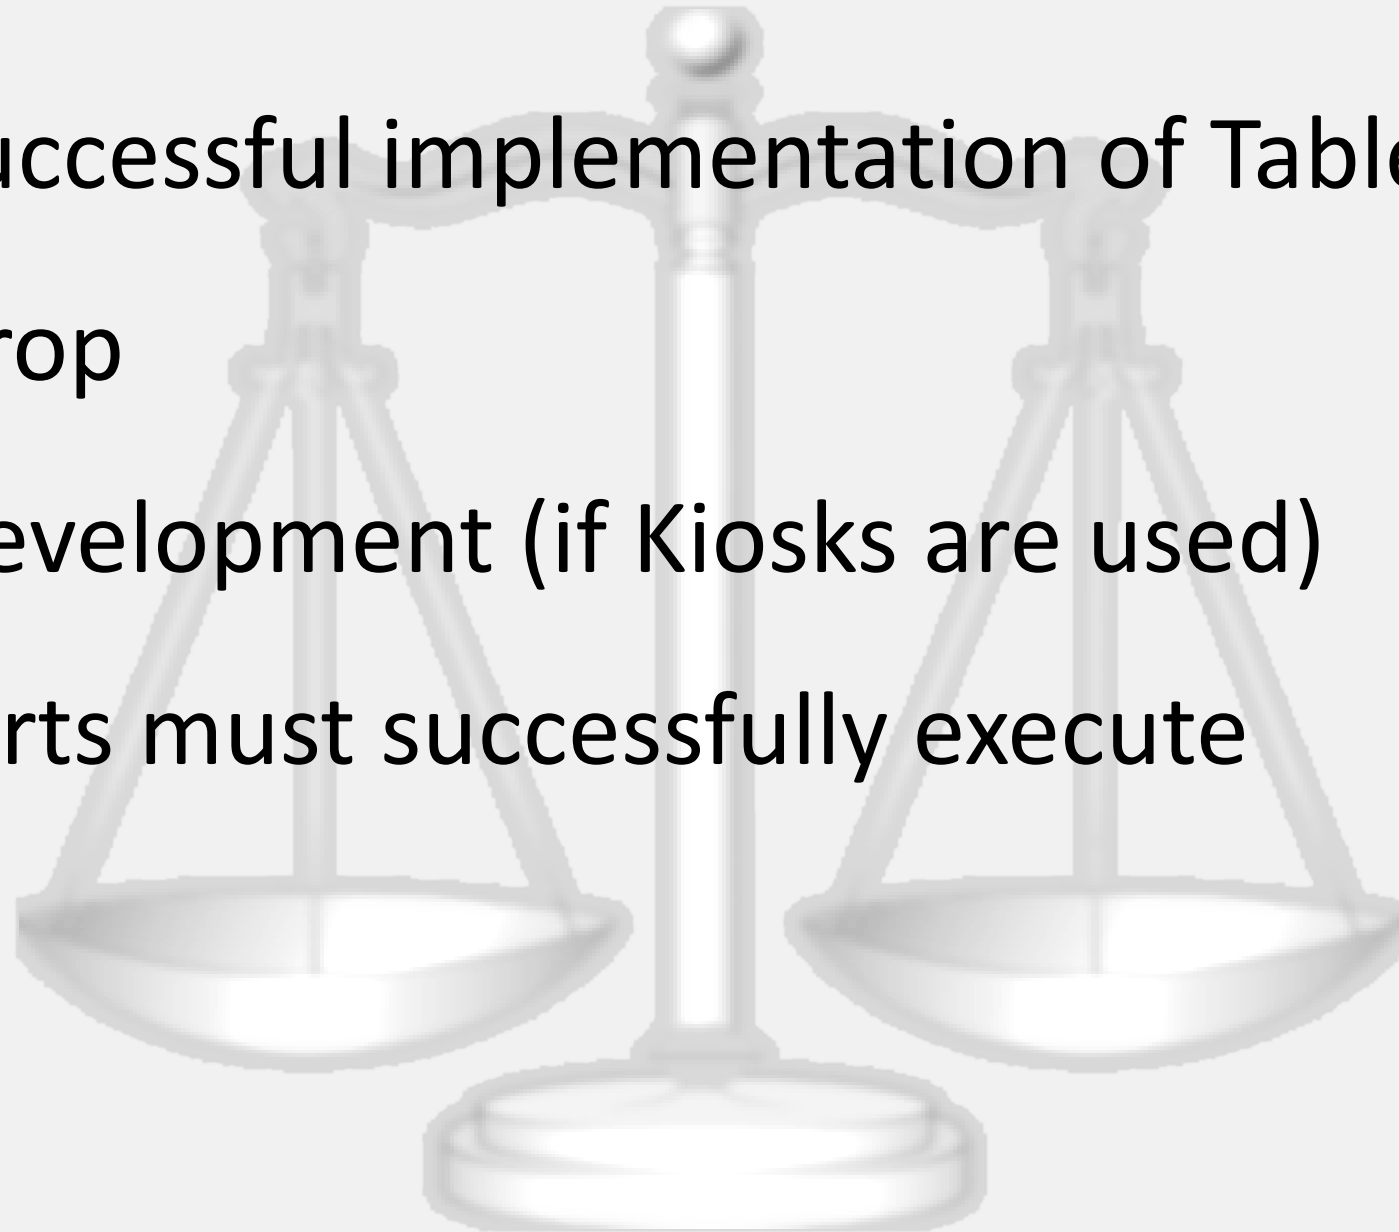

What Constitutes “Completion”

- Successful Installation and Testing of AgileJury 4.4
- Date: April 20, 2018

