ID	Task Name
1	**RFR Project**
2	Project Funding Approval by COT (Nov 2004, see notes)
3	**Gap Analysis of iCIS Juvenile and Adult RFR**
7	**Business Process Analysis and Requirements Phase**
8	**Business Process Analysis**
61	**Process Decomposition**
71	**Business Requirements**
76	Estimate Development, QA, Data Conversion, User Acceptance, Im
77	Review/Approve BPR
78	Process Analysis / Requirements Complete
79	**System Design Phase**
80	**.Net Development framework**
98	**Detailed System Design, Specifications (3 people)**
99	**Conceptual Design (iterative process)**
114	Database Design
115	Refined Project Plan
116	Develop system design
117	Elicit Business Rules
118	Proposed Business Process Modification
119	Write programming Specifications
120	Review/revise system design/Programming Specifications
121	Design Complete
122	**Construction**
123	**Conversion**
170	**Foundation**
481	**Reports Foundation**
543	**Case**
681	**Obligation**
808	**Disbursement**
969	**Review Action Screen**
973	**My Dash Board**
990	**Civil Judgment**
1069	**APD**
1106	**Integration**
1179	**Jobs**
1215	**Reports**
1330	Construction Complete
1331	**QA testing**
1378	**Performance Tuning - Applications**
1382	**Performance Tuning - Reports**
1386	**User Acceptance testing - Screens**
1390	**User Acceptance testing - Reports**
1394	Training
1395	Implementation
1396	Project complete

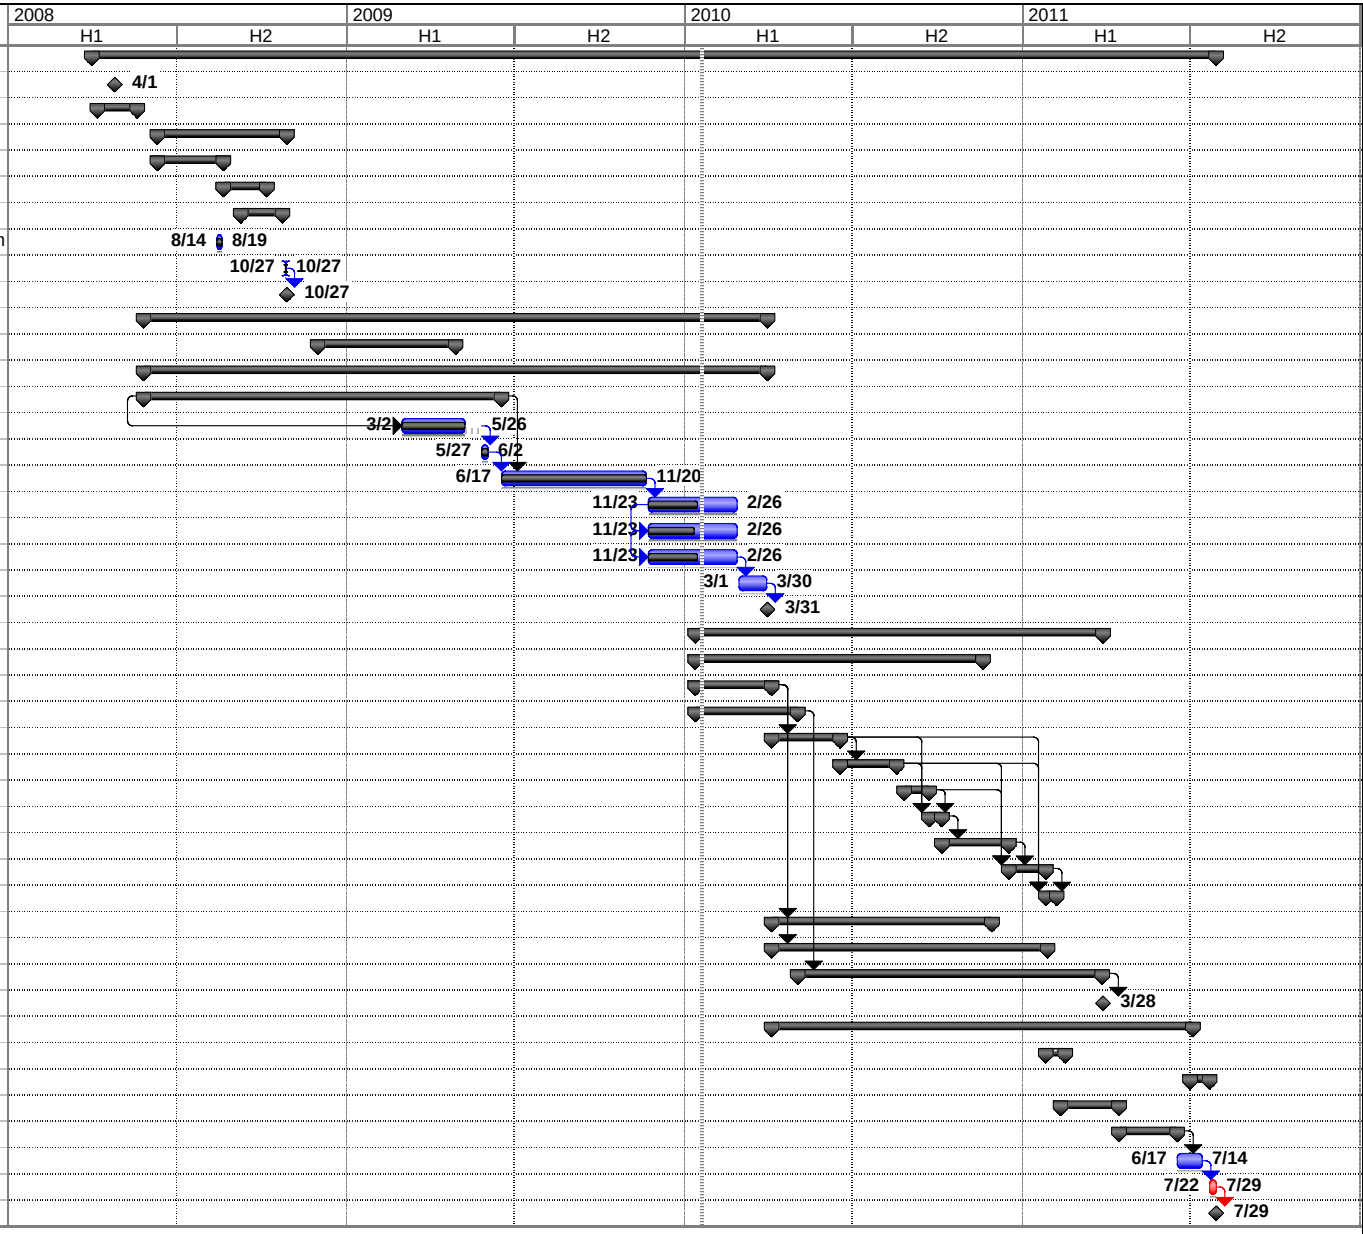

Project: RFR_Estimate_2009-12-18_lo
Date: Tue 1/19/10

Task	Summary	Rolled Up Progress	Group By Summary
Critical Task	Rolled Up Task	Split	Deadline
Progress	Rolled Up Critical Task	External Tasks	
Milestone	Rolled Up Milestone	Project Summary	
