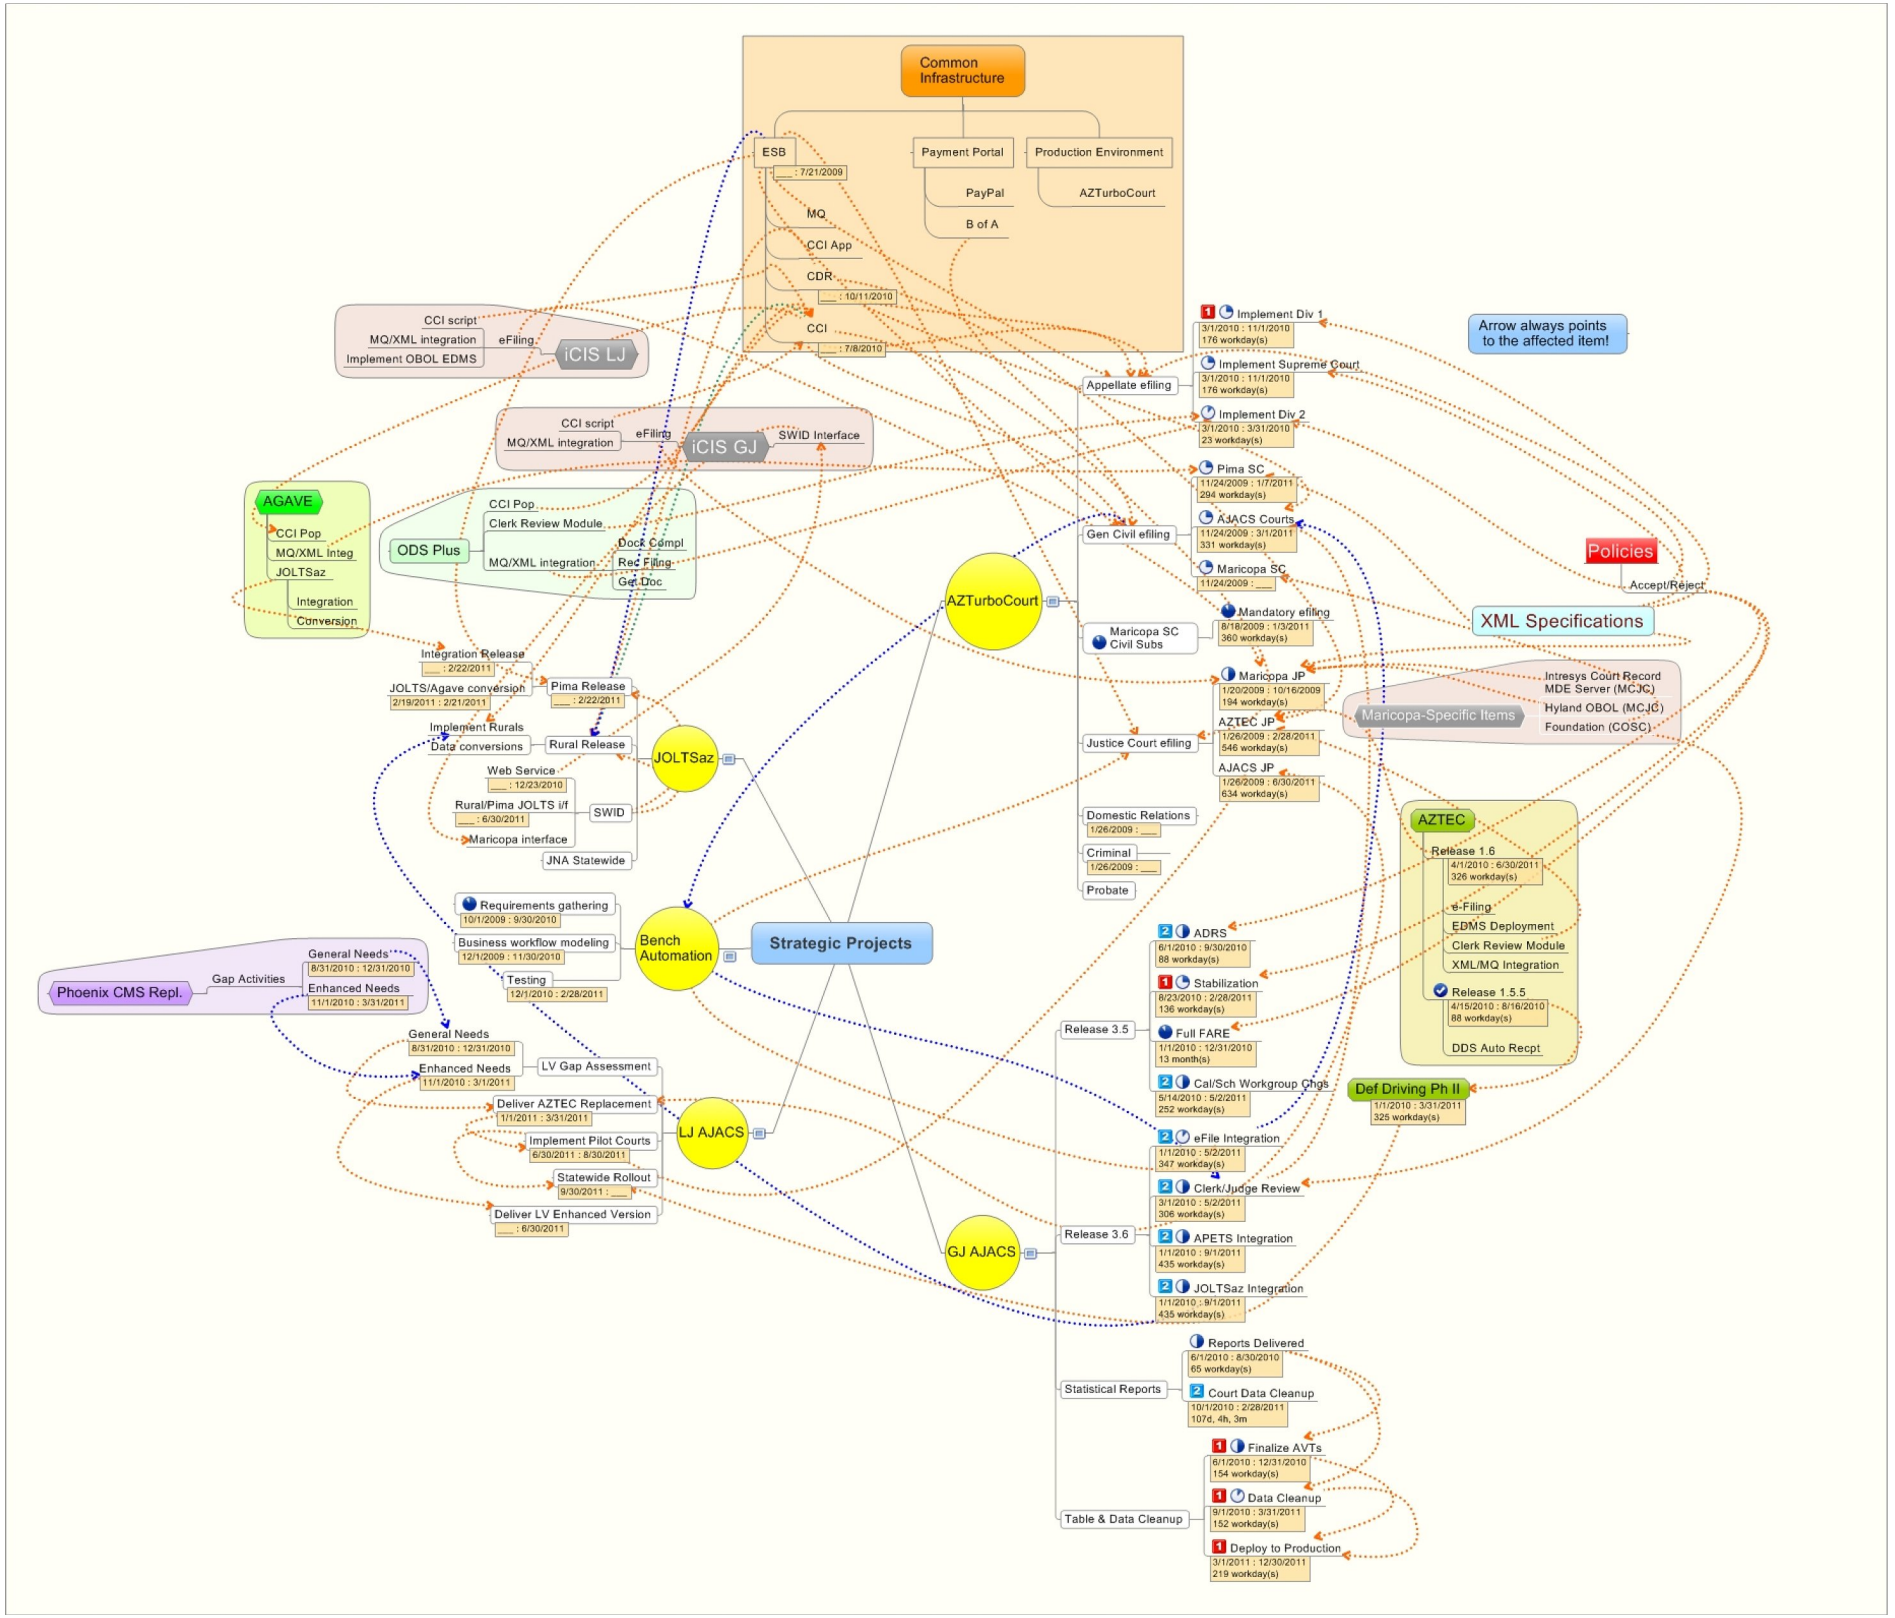
Common Infrastructure
ESB
___ : 7/21/2009
MQ
CCI App
CDR
___ : 10/11/2010
CCI
___ : 7/8/2010
Payment Portal
PayPal
B of A
Production Environment
AZTurboCourt
iCIS LJ
CCI script
MQ/XML integration
Implement OBOL EDMS
eFiling
iCIS GJ
CCI script
MQ/XML integration
eFiling
SWID Interface
AGAVE
CCI Pop
MQ/XML Integ
JOLTSaz
Integration
Conversion
ODS Plus
CCI Pop
Clerk Review Module
MQ/XML integration
Dock Compl
Rec Filing
Get Doc
Integration Release
___ : 2/22/2011
JOLTS/Agave conversion
2/19/2011 : 2/21/2011
Pima Release
___ : 2/22/2011
Implement Rurals
Data conversions
Rural Release
Web Service
___ : 12/23/2010
Rural/Pima JOLTS i/f
___ : 6/30/2011
SWID
Maricopa interface
JNA Statewide
JOLTSaz
Requirements gathering
10/1/2009 : 9/30/2010
Business workflow modeling
12/1/2009 : 11/30/2010
Testing
12/1/2010 : 2/28/2011
Bench Automation
Strategic Projects
Phoenix CMS Repl.
Gap Activities
General Needs
8/31/2010 : 12/31/2010
Enhanced Needs
11/1/2010 : 3/31/2011
General Needs
8/31/2010 : 12/31/2010
Enhanced Needs
11/1/2010 : 3/1/2011
LV Gap Assessment
Deliver AZTEC Replacement
1/1/2011 : 3/31/2011
Implement Pilot Courts
6/30/2011 : 8/30/2011
Statewide Rollout
9/30/2011 : ___
Deliver LV Enhanced Version
___ : 6/30/2011
LJ AJACS
AZTurboCourt
GJ AJACS
Appellate efiling
Implement Div 1
3/1/2010 : 11/1/2010
176 workday(s)
Implement Supreme Court
3/1/2010 : 11/1/2010
176 workday(s)
Implement Div 2
3/1/2010 : 3/31/2010
23 workday(s)
Gen Civil efiling
Pima SC
11/24/2009 : 1/7/2011
294 workday(s)
AJACS Courts
11/24/2009 : 3/1/2011
331 workday(s)
Maricopa SC
11/24/2009 : ___
Maricopa SC Civil Subs
Mandatory efiling
8/18/2009 : 1/3/2011
360 workday(s)
Justice Court efiling
Maricopa JP
1/20/2009 : 10/16/2009
194 workday(s)
AZTEC JP
1/26/2009 : 2/28/2011
546 workday(s)
AJACS JP
1/26/2009 : 6/30/2011
634 workday(s)
Domestic Relations
1/26/2009 : ___
Criminal
1/26/2009 : ___
Probate
Arrow always points to the affected item!
Policies
Accept/Reject
XML Specifications
Maricopa-Specific Items
Intresys Court Record MDE Server (MCJC)
Hyland OBOL (MCJC)
Foundation (COSC)
AZTEC
Release 1.6
4/1/2010 : 6/30/2011
326 workday(s)
e-Filing
EDMS Deployment
Clerk Review Module
XML/MQ Integration
Release 1.5.5
4/15/2010 : 8/16/2010
88 workday(s)
DDS Auto Recpt
Def Driving Ph II
1/1/2010 : 3/31/2011
325 workday(s)
Release 3.5
ADRS
6/1/2010 : 9/30/2010
88 workday(s)
Stabilization
8/23/2010 : 2/28/2011
136 workday(s)
Full FARE
1/1/2010 : 12/31/2010
13 month(s)
Cal/Sch Workgroup Chgs
5/14/2010 : 5/2/2011
252 workday(s)
Release 3.6
eFile Integration
1/1/2010 : 5/2/2011
347 workday(s)
Clerk/Judge Review
3/1/2010 : 5/2/2011
306 workday(s)
APETS Integration
1/1/2010 : 9/1/2011
435 workday(s)
JOLTSaz Integration
1/1/2010 : 9/1/2011
435 workday(s)
Statistical Reports
Reports Delivered
6/1/2010 : 8/30/2010
65 workday(s)
Court Data Cleanup
10/1/2010 : 2/28/2011
107d, 4h, 3m
Table & Data Cleanup
Finalize AVTs
6/1/2010 : 12/31/2010
154 workday(s)
Data Cleanup
9/1/2010 : 3/31/2011
152 workday(s)
Deploy to Production
3/1/2011 : 12/30/2011
219 workday(s)
